YOUR LOGO

Your Company Name

Your phone · Your license


Quote, Rev A
October 9, 2026

Job location

Project
Basement finish

Walk-around stairs

Two bedrooms, a full bath and a living area.

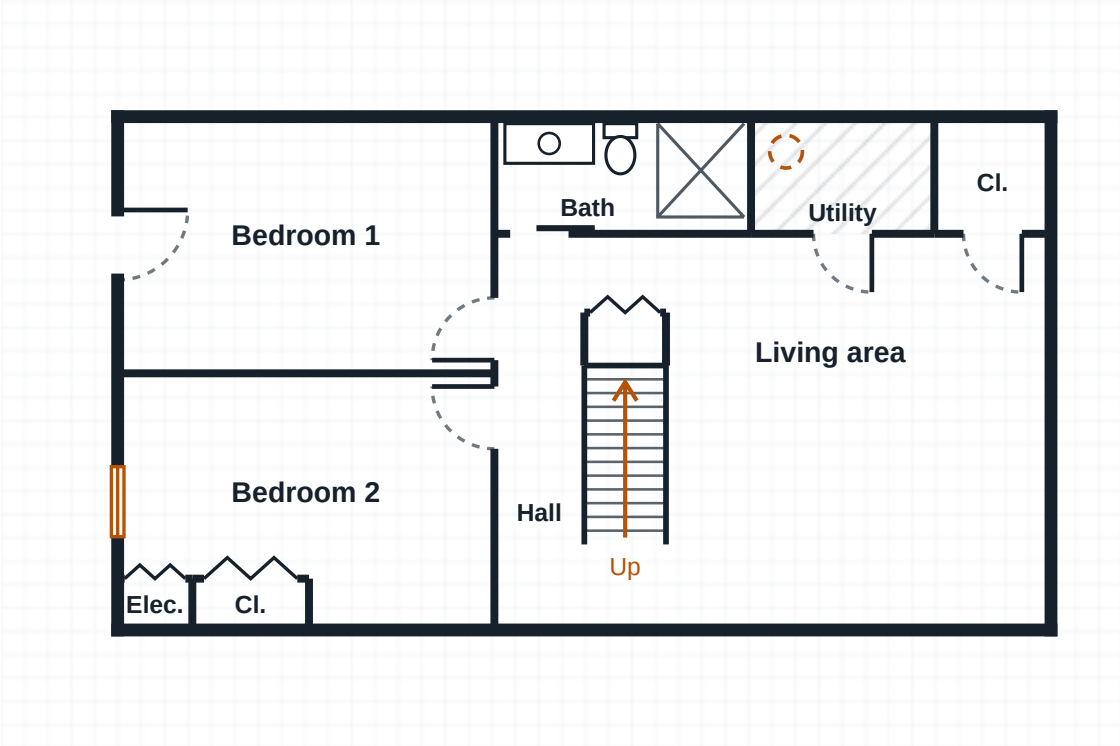

Floor plan

Work included

General conditions
Debris removal, material delivery, floor protection during the work and a final cleaning. Removal of the old stud wall.

Framing
Frame all new walls on pressure-treated plates, with soffits around ducts and beams, and a finished shelf along the foundation ledge.

Insulation
1 in. foam board (R-5) on the foundation walls, R-13 batt insulation in the outside stud walls, sound insulation in the interior walls and rim joist insulation.

Drywall and ceiling
Blueboard on all new walls and the ceiling with a smooth veneer plaster finish by a plasterer, moisture-resistant board in the bath.

Work included

Paint
Primer and two finish coats on walls, ceiling, doors and trim.

Flooring
A plastic vapor barrier over the sealed slab and install the click-lock plank flooring, in the bathroom too.

Doors, trim and stairs
Hang the interior doors, a pocket door at the bath, closet doors, casing and baseboard, closet shelf and rod, a closet with its own door around the electrical panel, wood wraps with base trim on the support poles, new stair treads and risers with new railing, a new window in the existing bedroom opening, a new outside door and screen door at Bedroom 1 and louvered doors at the equipment closets.

Electrical
Outlets placed to code, install recessed lights on dimmers, closet, utility and stair lights, switches, hardwired smoke and CO alarms, bath fan, an electric baseboard heater in the bathroom, power and cable plugs behind the TV with the TV mount hung on blocking and new circuits with arc-fault and ground-fault protection.

Plumbing
Full bathroom: drain and water piping, and installation of the toilet, vanity, shower and accessories. A sewage ejector pump in a sealed basin lifts the bath drains to the house drain line.

HVAC
Bath fan ducted to the outside.

Concrete and slab work
Cut the slab for the bath drains and the pump pit, then backfill and patch the concrete. Clean and patch the foundation walls and slab before the waterproofing goes on. Repair the cracks in the slab and the foundation wall.

Project management
Project management and office time: scheduling and ordering, and your single point of contact.

Site supervision
A supervisor on site running the crew and checking the work.

Base price, labor and installation included [redacted]

Your selections	Material allowance
Recessed light fixtures Allows [redacted] per fixture.	[redacted]
Click-lock plank flooring Allows [redacted] per square foot.	[redacted]
Vanity, top and faucet	[redacted]
Shower unit, valve and trim	[redacted]
Toilet	[redacted]

Your selections	Material allowance
TV wall mount Hanging system for one TV. Hanging it is in the base price.	[redacted]
Vanity light	[redacted]
Closet system under the stairs Shelving, rods and doors built in under the stairs. Building it in is in the base price.	[redacted]
Interior doors and hardware Allows [redacted] per door.	[redacted]
Material allowances	[redacted]

These are budgets for materials you choose. If you pick something that costs more or less, the price changes by the difference in material only. Installation is already in the base price and does not change.

Total [redacted]

Add alternates	Price
Mini-split heating and cooling, installation 3 indoor units and one outdoor unit, mounted, wired and started up, with 28 ft of line to each. Separate from the existing heating system, which is not touched. If this option is not chosen, heating and cooling for the new rooms are done by others.	[redacted]
Mini-split equipment, material allowance Value-grade system. A different unit changes this amount only.	[redacted]
Subfloor panels Insulated raised subfloor panels under the flooring, in place of the plastic vapor barrier. A warmer floor and a second moisture break.	[redacted]
Total with both add alternates	[redacted]

Payment schedule

Deposit, to order materials Covers the materials for the job. Due at signing.	[redacted]
At the start of work	[redacted]
When rough-in is complete Framing, wiring, plumbing and heating are in and inspected, before the walls are closed.	[redacted]
At completion	[redacted]

If the add alternate is chosen, its equipment is added to the deposit and its installation is split across the three payments.

Terms

- About 43 working days on site.
- Good for 30 days from the date above.
- Permits: any permits, permit fees and inspections for this work are obtained and paid for by the customer. They are not part of this price.
- Heating and cooling: if the mini-split option is not chosen, heating and cooling for the new rooms are done by others.
- Changes: any change to this scope is written up and priced, and approved by you, before that work is done.
- Warranty: workmanship is warranted for one year from completion. Products carry their makers' warranties.
- Your part: the basement cleared before the start date, access to the house on work days, and selections made within one week of signing.
- This estimate, its drawings and its scope of work were prepared by Your Company Name for this customer and this job. They are not to be copied, shared or used to obtain other bids.

Not included

Furniture and window treatments. Septic system work. Engineering and design fees. Electrical panel or service upgrade, if one is required. Repair of hidden conditions such as water, mold or structural damage.

Accepted by

Date
